Weekly Progress Status Report

USH 45/STH 100 (108th Street) College Avenue to Edgerton Avenue 2040-11-70

Past Week:

- Removals and grading:
 - Placed topsoil on east side of Hwy 100
 - o Graded and placed base aggregate along Hwy 100 from Rockne Ave to Grange Ave

Week Ending October 5, 2018

- Storm sewer:
 - o Installed storm sewer trunk line between Grange Ave to Copeland Ave
 - o Installed storm sewer laterals along Hwy 100 from Parnell Ave to Grange Ave
- Electrical
 - Installed conduit, bases and, pullboxes at the east leg of Edgerton Ave.
 - o Installed conduit, bases and, pullboxes at the NE corner of Hwy 100 & Janesville Rd.
- Structures:
 - o Box culvert (B-40-408) extension: dewatering of site due to heavy rains
- Paving:
 - Placed surface layer of asphaltic pavement on the east legs of Janesville Rd & Forest Home Ave.
 - Placed asphaltic pavement for driveways and parking lots on the east legs of Janesville Rd & Forest Home Ave.
 - Placed asphaltic pavement for driveways and parking lots from Kay Ave to south project limits.
- Permanent Signs:
 - Placed permanent roadway signs along the east legs of Janesville Rd & Forest Home Ave.
- Miscellaneous Tasks:
 - o Maintenance of traffic control devices.
 - o Maintenance of erosion control devices.
- Utilities: adjustments/relocates of telecommunication, water, gas, & electrical facilities as needed

Upcoming week

- o Structure: Continue construction of south cell extension walls and wingwall.
- Electric: Signal & light bases, conduit, pull boxes east side of Hwy 100
- Storm Sewer: Continue installation of storm sewer from Grange Ave to Copeland Ave.
- Concrete: Continue sidewalk and pedestrian curb from Edgerton to Copeland Place curb and gutter between Scharles Ave and Grange Ave.
- Grading: Prep terrace areas and continue placing topsoil behind sidewalk
 Excavate and place base aggregate on the north half of Grange Ave.
- Paving: Place top layer of asphaltic pavement on Hwy 100 from Kay Pkwy to south limit.
 Place top layer of asphaltic pavement on Hwy 100 between Janesville Rd and Forest Home Ave

Weekly Progress Status Report

USH 45/STH 100 (108th Street) College Avenue to Edgerton Avenue 2040-11-70

Week Ending October 5, 2018

- o Round About Closure (east legs of Janesville Rd & Forest Home Ave)
 - Grading: Continue placing topsoil behind sidewalk for final restoration
 - Electrical: Begin installation of light poles
 - Concrete: Complete miscellaneous concrete crosswalk and sidewalk sections
 Signs: Install overhead sign supports.
 - Pavement Marking: Install permanent lane lines, crosswalks, and lane designation symbols

Construction Photos



Installation of erosion control devices at the project fill site.

Weekly Progress Status Report

USH 45/STH 100 (108th Street) College Avenue to Edgerton Avenue 2040-11-70

Week Ending October 5, 2018



Adjusting storm sewer inlet elevation in preparation for curb & gutter.




Installation of storm sewer inlets and lateral connection pipes along Hwy 100 south of Grange Ave.

Weekly Progress Status Report USH 45/STH 100 (108th Street)

USH 45/STH 100 (108th Street) College Avenue to Edgerton Avenue 2040-11-70

Week Ending October 5, 2018



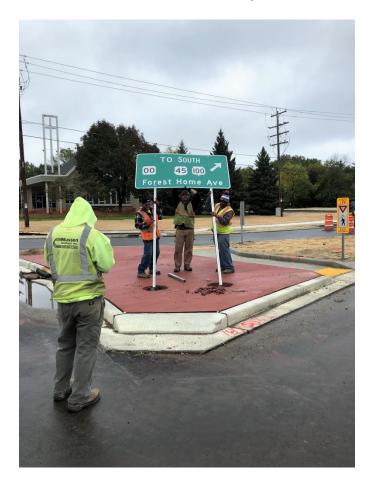

Installation of permanent signs in the round-about median Islands of Janesville Rd. & Forest Home Ave.

Weekly Progress Status Report USH 45/STH 100 (108th Street)

USH 45/STH 100 (108th Street) College Avenue to Edgerton Avenue 2040-11-70

Week Ending October 5, 2018



Placement of the surface layer of asphaltic pavement on the east legs of Janesville Rd. & Forest Home Ave.
